SJSM · SATARA

PROJECT COMPLETION REPORT

INTEGRATED WATERSHED MANAGEMENT

Climate Resilience & Sustainable Livelihoods

LOCATION VELOSHI, BLOCK – PHALTAN, DIST. SATARA

PERIOD JANUARY 2026– MARCH 2026

"Supported by"
PARIVARTAN
A step towards sustainable progress

"Anchored by"
Bharat Cares ®
by SMEC Trust

SHRAMJIVI
Empowering India

Shramjivi Janata Sahayyak Mandal

CONTENTS

Table of Contents

01	Executive Summary	3
02	Project Overview & Background	4
03	Objectives & Scope	4
04	Key Interventions & Approach	5
05	Key Achievements & Milestones	6
06	Outcomes & Impact	7
07	Challenges & Mitigation	8
08	Lessons Learned	8
09	Sustainability & Roadmap	8
10	Monitoring & Evaluation	9
11	Events & Campaigns	9
12	Case Studies & Success Stories	10
13	Community Feedback	10
14	Field Photography	11

EXECUTIVE *Summary*

98	18	100%	38,000
HOUSEHOLDS	ACRES	COMPLETE	M^3
DIRECT BENEFICIARIES	LAND RECLAIMED	ALL 6 TARGETS MET	TOTAL EARTHWORK

THE PROJECT REACHED A FINAL MILESTONE DURING JANUARY–MARCH 2026 WITH 100% EXECUTION OF ALL PROPOSED PRIMARY ACTIVITIES. ALL STRUCTURAL AND EARTHWORK INTERVENTIONS MET THEIR TARGETS, PROVIDING IMMEDIATE AGRICULTURAL BENEFITS — LAND RECLAMATION AND ENHANCED WATER STORAGE — FOR THE FARMING COMMUNITY OF VELOSHI.

Soil Conservation

1 Gabion + 15 Loose Boulder structures fully completed, protecting watershed integrity.

Land Reclamation

18 acres of barren land converted to fertile farmland using nutrient-rich desilted soil.

Water Management

38,000 m³ of Nala deepening and desilting achieved, improving drainage and storage.

Community Impact

98 farming families are directly & 72 indirectly benefiting from improved land and water access.



PROJECT OVERVIEW & BACKGROUND

LOCATION	PERIOD
Veloshi, Block Phaltan Dist. Satara Maharashtra	**January – March 2026** (*Final Reporting*)

BACKGROUND & CONTEXT

SHRAMJIVI JANATA SAHAYYAK MANDAL (SJSM) IS A REGISTERED NGO BASED IN SATARA, MAHARASHTRA, COMMITTED TO INTEGRATED WATERSHED DEVELOPMENT AND RURAL LIVELIHOOD SUPPORT. SUPPORTED BY THE PARIVARTAN SMALL GRANTS PROGRAMME OF HDFC BANK, THIS INITIATIVE RESTORES THE WATERSHED IN VELOSHI VILLAGE — A RAIN-FED AGRICULTURAL COMMUNITY VULNERABLE TO MONSOON VARIABILITY.

PROJECT SCOPE

- Geographic focus on Veloshi, Satara watershed
- Gabion & Loose Boulder construction for soil conservation
- Nala deepening/widening and ENB desilting
- Land reclamation through desilted soil distribution
- Farmer Exposure Visit for community knowledge transfer

BENEFICIARY PROFILE

98

HOUSEHOLDS

DIRECTLY BENEFITING FROM SOIL DISTRIBUTION & LAND PREP









KEY INTERVENTIONS & APPROACH

01 GABION STRUCTURES

TARGET: 1 NO. ACHIEVED: 1 NO.

WIRE-MESH ROCK STRUCTURES BUILT TO STABILISE STREAM BANKS, REDUCE WATER VELOCITY, AND PREVENT DOWNSTREAM EROSION — ESPECIALLY CRITICAL DURING MONSOON FLOODS.

02 LOOSE BOULDER STRUCTURES

TARGET: 15 NO. ACHIEVED: 15 NO.

FIFTEEN PERMEABLE CHECK DAMS PLACED ACROSS SEASONAL STREAMS TO SLOW WATER FLOW, ENCOURAGE INFILTRATION, AND REDUCE SOIL LOSS FROM SLOPED AGRICULTURAL FIELDS.

03 STAGGERED CONTOUR TRENCHES

TARGET: 4,500 M³ ACHIEVED: 4,500 M³

TRENCHES DUG ACROSS HILL SLOPES CAPTURE RAINWATER FOR PERCOLATION, ENHANCING GROUNDWATER RECHARGE AND PROVIDING MOISTURE TO VEGETATION THROUGH DRY PERIODS.

04 NALA DEEPENING & WIDENING

TARGET: 19,000 M³ ACHIEVED: 19,000 M³

DEEPENING AND WIDENING OF SEASONAL STREAMS TO IMPROVE WATER CARRYING CAPACITY, STORAGE, AND DRAINAGE — REDUCING FLOOD RISK AND EXTENDING WATER AVAILABILITY.

05 DESILTING OF WATER BODIES

TARGET: 19,000 M³ ACHIEVED: 19,000 M³

EXISTING WATER BODIES WERE DESILT ED TO RESTORE CAPACITY. NUTRIENT-RICH EXCAVATED SOIL WAS REDISTRIBUTED TO RECLAIM 18 ACRES OF BARREN AGRICULTURAL LAND.

06 FARMER EXPOSURE VISIT

TARGET: 1 VISIT ACHIEVED: 1 VISIT

STRUCTURED FIELD VISIT TO VILLAGE GHATDARE DEMONSTRATED BEST PRACTICES IN WATERSHED MANAGEMENT, BUILDING LOCAL CAPACITY FOR ONGOING MAINTENANCE AND REPLICATION.

100% TARGETS MET


Every planned intervention completed on time — meeting or exceeding all targets.

Activity / Intervention	Target	Achieved	Status
Gabion Structures	1 No.	1 No.	100%
Loose Boulder Structures (LB)	15 No.	15 No.	100%
Staggered Contour Trenches (SCT)	4,500 m³	4,500 m³	100%
Desilting of Small ENB	19,000 m³	19,000 m³	100%
Nala Deepening & Widening	19,000 m³	19,000 m³	100%
Farmer Exposure Visit	1 Visit	1 Visit	100%

> *"EVERY WATERSHED INTERVENTION FULLY DELIVERED ON TIME — A MILESTONE REFLECTING THE ENTIRE TEAM'S DEDICATION TO CLIMATE-RESILIENT DEVELOPMENT."*

16	38,000	4,500	18 ACRES
STRUCTURES BUILT	M³ EARTHWORK	M³ SCT	RECLAIMED

Achievement Rate

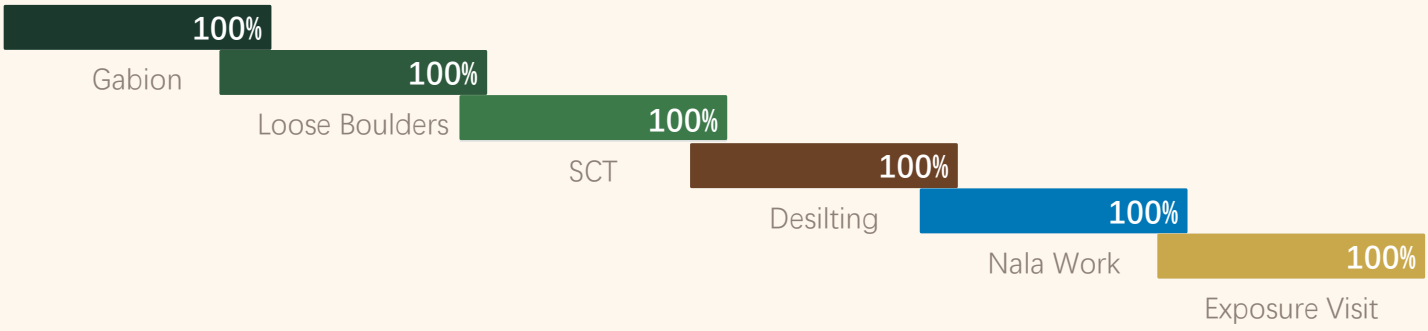


Nala Deepening Work



Desilted Soil Distribution

TRANSFORMING LAND, WATER & LIVES

18	98	19,000	19,000	4,500
ACRES	HOUSEHOLDS	M³	M³	M³
BARREN LAND CONVERTED TO CULTIVABLE FARMLAND	DIRECT BENEFICIARIES FROM DESILTED SOIL	NALA DEEPENING & WIDENING COMPLETED	DESILTING OF EXISTING WATER BODIES	CONTOUR TRENCHES CONSTRUCTED

LAND RECLAMATION

THROUGH 19,000 M³ OF DESILTING, NUTRIENT-RICH SOIL WAS DISTRIBUTED ACROSS 18 ACRES OF BARREN LAND, DIRECTLY EXPANDING THE CULTIVABLE AREA FOR 98 BENEFICIARY FAMILIES.

CLIMATE RESILIENCE

PRE-MONSOON COMPLETION OF ALL GABIONS, LOOSE BOULDERS, AND SCT MEANS THE WATERSHED NOW HARVESTS AND RETAINS RAINFALL, REDUCING RUNOFF AND REPLENISHING GROUNDWATER RESERVES.

WATER INFRASTRUCTURE

COMBINED NALA DEEPENING AND DESILTING (38,000 M³ TOTAL) HAS DRAMATICALLY IMPROVED DRAINAGE AND WATER STORAGE ACROSS THE VELOSHI WATERSHED, REDUCING FLOOD RISK AND EXTENDING IRRIGATION ACCESS.

COMMUNITY EMPOWERMENT

THE FARMER EXPOSURE VISIT EQUIPPED LOCAL STAKEHOLDERS WITH HANDS-ON WATERSHED KNOWLEDGE. WATER USER GROUP FORMATION WILL ENSURE COMMUNITY-LED MAINTENANCE OF ALL COMPLETED INFRASTRUCTURE.

EVENTS & FIELD CAMPAIGNS



PROJECT INAUGURATION

ON FEBRUARY 3, 2026, THE PROJECT WAS INAUGURATED AT VELOSHI VILLAGE IN PHALTAN BLOCK, WITH VILLAGERS AND SJSM MEMBERS IN ATTENDANCE.



LAND RECLAMATION DRIVE

VELOSHI, BLOCK PHALTAN, SATARA

AWARENESS CAMPAIGN ON THE BENEFITS OF USING NUTRIENT-RICH DESILTED SOIL FOR FARMLAND RECLAMATION. ALL 98 BENEFICIARY HOUSEHOLDS WERE REACHED WITH GUIDANCE ON LAND PREPARATION AND CROP SELECTION FOR NEWLY CONVERTED 18-ACRE PLOTS.

CHALLENGES, LESSONS & FUTURE ROADMAP

CHALLENGE ENCOUNTERED & OVERCOME

FINALISING THE LAST 1,500 M³ OF NALA DEEPENING WITHIN THE REPORTING DEADLINE REQUIRED INTENSIVE DAILY MONITORING AND FIELD EXECUTION BY SITE SUPERVISORS. THROUGH SUSTAINED EFFORT, 100% OF THE TARGETED 19,000 M³ WAS ULTIMATELY ACHIEVED.

WHAT WORKED

INTEGRATION OF DESILTING WITH LAND RECLAMATION CONVERTED 18 ACRES OF BARREN LAND. PRE-MONSOON STRUCTURAL COMPLETION ENSURED IMMEDIATE WATER HARVESTING BEFORE RAINS ARRIVED.

WHAT COULD IMPROVE

A SINGLE FARMER EXPOSURE VISIT LIMITS DEEP KNOWLEDGE TRANSFER. MORE FREQUENT COMMUNITY ENGAGEMENT SESSIONS WOULD ENHANCE ADOPTION OF WATERSHED MANAGEMENT TECHNIQUES.

RECOMMENDATIONS

FUTURE PROJECTS SHOULD SOIL-TEST DESILTED MATERIAL BEFORE DISTRIBUTION TO OPTIMISE CROP SELECTION. FORM WATER USER GROUPS FOR LONG-TERM MAINTENANCE OF ALL COMPLETED STRUCTURES.

SUSTAINABILITY & FUTURE ROADMAP

SR. NO.	COMPONENT	DESCRIPTION	KEY FOCUS AREA
01	**CAPACITY BUILDING**	CONDUCTED TRAINING FOR ALL 28 BENEFICIARY HOUSEHOLDS ON SUSTAINABLE AGRICULTURE AND SOIL MANAGEMENT FOR NEWLY RECLAIMED LAND.	FARMER TRAINING & SOIL SUSTAINABILITY
02	**COMMUNITY OWNERSHIP**	ESTABLISHED WATER USER GROUPS FROM LOCAL FARMING COMMUNITIES TO ENSURE LONG-TERM MAINTENANCE OF WATERSHED STRUCTURES.	LOCAL GOVERNANCE & MAINTENANCE
03	**SCALE & CONTINUITY**	EXPANDED THE NALA DEEPENING MODEL TO ADJACENT WATERSHEDS IN PHALTAN BLOCK, REPLICATING 19,000 M³ EARTHWORK APPROACH.	MODEL REPLICATION & EXPANSION

MONITORING & EVALUATION

MECHANISM	FREQUENCY	RESPONSIBLE	KEY FINDING
FIELD VISITS	REGULAR	MR. SURESH KADAM (PM)	VERIFIED SCT & DESILTING COMPLETION
WEEKLY UPDATES	WEEKLY	SITE SUPERVISORS	TRACKED NALA WIDENING TO 19,000 M³
DASHBOARDS	MONTHLY	PROJECT MGMT. UNIT	PROGRESS VS ALL 6 TARGETS VISUALISED
PROGRESS RPTS	MONTHLY	REPORTING TEAM	FEB–MAR 2026 ACHIEVEMENTS COMPILED
AUDIT	END-OF-PROJECT	FINANCIAL AUDITOR	ALIGNED WITH PARIVARTAN SGP GUIDELINES

SUCCESS STORIES & COMMUNITY VOICES



TRANSFORMING BARREN LAND

into Productive Farmland

In Veloshi village, what was once infertile rocky land now sustains crops for 39 farming families. Through 19,000 m³ of strategic desilting, the project restored water bodies and unlocked 18 acres of agricultural potential. Nutrient-rich sediment, carefully redistributed, has transformed the soil profile of barren plots, giving each family a direct stake in the watershed's recovery.

Land Reclamation | Water Conservation | 98 Beneficiaries | Satara

The structural and earthwork interventions have successfully met their primary targets, resulting in immediate agricultural benefits for our community.

Chandrakant Jadhav
Sarpanch, Veloshi

18 acres of previously barren land have been transformed into cultivable agricultural land — a life-changing outcome for our families.

Sunil Mane
Benefited Farmer, Veloshi

All proposed activities — Gabions, SCT, and Nala work — were fully executed on time. A remarkable achievement in watershed management.

Ram Kolekar
Head Operations SJSM.

PROJECT IN ACTION















DRONE PHOTOGRAPHS















EARTHWORK, LAND & COMMUNITY



Desilted Soil Distribution



Land Levelling



Reclaimed Agricultural Land



Gabion Structure



Exposure Visit to Ghatdare, Khandala Block



Structure Signage Board

THANK YOU

Shramjivi Janata Sahayyak Mandal (SJSM), Satara

Integrated Watershed Management for Climate Resilience & Sustainable Livelihoods

Project Completion Report2025–26 | Submitted: 30 March 2026

Veloshi, Block – Phaltan, Dist. Satara, Maharashtra

Reporting Period: January – March 2026 (Final)

Supported under the Parivartan Small Grants Programme 2025-2026

"Supported by" PARIVARTAN A step towards sustainable progress

SHRAMJIVI Empowering India

"Anchored by" Bharat Cares by SMEC Trust



Growing Communities · Conserving Water · Building Resilience
