SJSM · SATARA

ANNUAL REPORT FY 2025–26

TE INTEGRATED WATERSHED MANAGEMENT PROJECT *(IWMP)*

LOCATION GHATDARE, KHANDALA, DIST. SATARA

CSR Partner: TE CONNECTIVITY

TE connectivity

SHRAMJIVI
Empowering India



CONTENTS

Table of Contents

01	Executive Summary	3
02	Background & Need	4
03	Project Objectives & Scope	4
04	Water Conservation Structures – Progress & Achievement	5
05	Achievement vs Target — Visual	5
06	Annual Water Storage Created by Structure	5
07	Outcomes & Measured Impact	6
08	Groundwater Monitoring — June 2025 to April 2026	6
09	Field Documentation –Nala Deepening & Earthwork	7
10	Field Documentation -Aerial View	8 -9
11	Field Documentation -Launch & Community	10
12	Water Purification Unit -Safe Drinking Water	11
13	Media Coverage Newspaper Reports	12
14	Alignment with UN Sustainable Development Goals	13

EXECUTIVE *Summary*

THE TE INTEGRATED WATERSHED MANAGEMENT PROJECT (IWMP) AT GHATDARE VILLAGE, KHANDALA, SATARA — IMPLEMENTED BY SHRAMJIVI JANATA SAHAYYAK MANDAL (SJSM) UNDER THE CSR INITIATIVE OF TE CONNECTIVITY — HAS COMPLETED ITS FIRST FULL YEAR (FY 2025-26) WITH NEAR-100% ACHIEVEMENT ACROSS ALL PRIMARY TARGETS. THE PROJECT HAS DELIVERED TANGIBLE OUTCOMES: A 2.5–3.2 METRE RISE IN GROUNDWATER LEVELS, 136.43 TCM OF ADDITIONAL ANNUAL WATER STORAGE, AND SUCCESSFUL COMMUNITY MOBILISATION OF ALL 225 HOUSEHOLDS ACROSS 647 HECTARES.

225	647	136.43	3+ metres
HOUSEHOLDS	HECTARES	TCM/YEAR	MAX RISE
COMMUNITY REACHED	TOTAL PROJECT AREA	WATER STORAGE CREATED	GROUNDWATER RECHARGE

PROJECT OVERVIEW

Project Title	TE Integrated Watershed Management Project (IWMP), Village – Ghatdare
CSR Partner	TE Connectivity
Implementing Partner	Shramjivi Janata Sahayyak Mandal (SJSM), Satara
Location	Ghatdare, Taluka – Khandala, District Satara, Maharashtra
Project Launch	1 April 2025
Reporting Period	April 2025 – March 2026 (FY 2025-26)
Head Operations	Mr. Ram Kolekar
Total Area	647 Hectares
Households	225 Households | Gram Panchayat Ghatdare–Bhoslewadi

BACKGROUND & NEED



Ghatdare Village — Google Earth Satellite View (Pre-intervention)

Ghatdare village has historically faced **acute water scarcity**, declining groundwater levels, and severe soil erosion that reduced agricultural productivity and increased drought vulnerability.

TE Connectivity, in partnership with SJSM and Gram Panchayat Ghatdare–Bhoslewadi, launched this integrated watershed programme to:

- Restore the natural water balance
- Control soil erosion through ridge-to-valley treatment
- Bring 647 ha of farmland under assured irrigation
- Provide safe drinking water to 225 households
- Build climate resilience and improve crop productivity


PROJECT OBJECTIVES

Groundwater Recharge	Increase groundwater recharge and create decentralized water storage through nala deepening and contour trenches.
Soil Conservation	Control soil erosion through comprehensive ridge-to-valley treatment using gabion, loose boulder, and SCT structures.
Irrigation Expansion	Bring 250 hectares of farmland under assured irrigation, progressing toward 647 ha total area target.
Safe Drinking Water	Install and commission a water purification unit to provide clean drinking water to all 225 households.
Community Governance	Build climate resilience through community mobilisation, Gram Sabha approvals, and local ownership of infrastructure.


WATER CONSERVATION STRUCTURES – PROGRESS & ACHIEVEMENT

Sr.	Activity / Intervention	Plan (Target)	Actual (Achieved)	Water Storage (TCM/year)
2a	Deep SCT – Staggered Contour Trenches	375 Pits	375 Pits	18.75
2b	Nala Deepening & Widening	25,000 m³	24,990 m³	74.97
2c	Desilting of Existing Water Bodies (ENB)	9,635 m³	9,635 m³	28.91
2d	Gabion Structures	5 Nos	5 Nos	7.50
2e	Loose Boulder Structures (LBS)	30 Nos	30 Nos	6.30
	TOTAL ANNUAL WATER STORAGE	–	–	**136.43 TCM**

ACHIEVEMENT VS TARGET — VISUAL

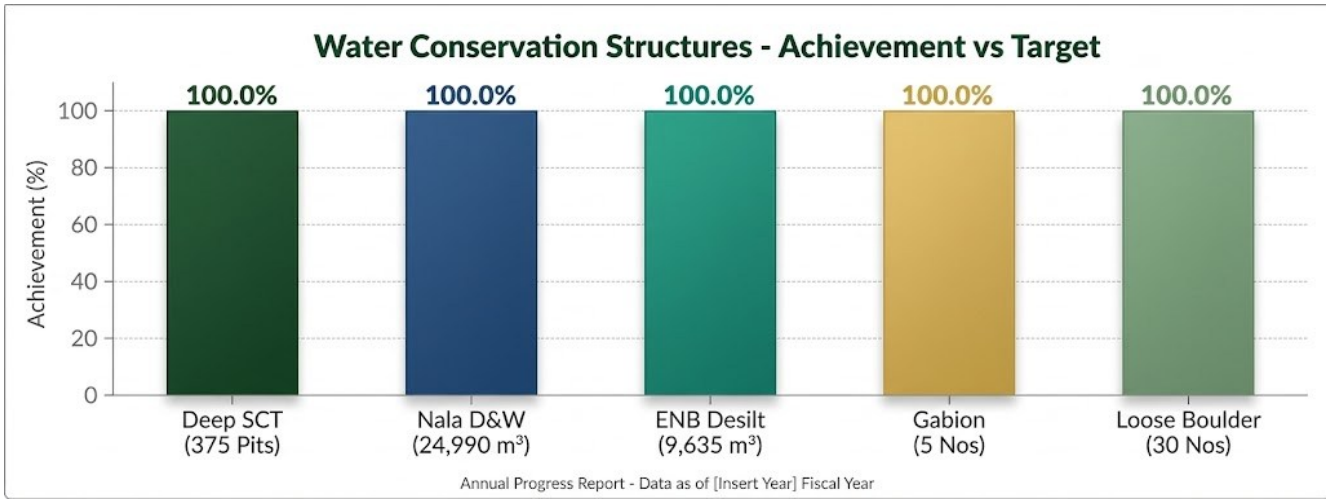


ANNUAL WATER STORAGE CREATED BY STRUCTURE

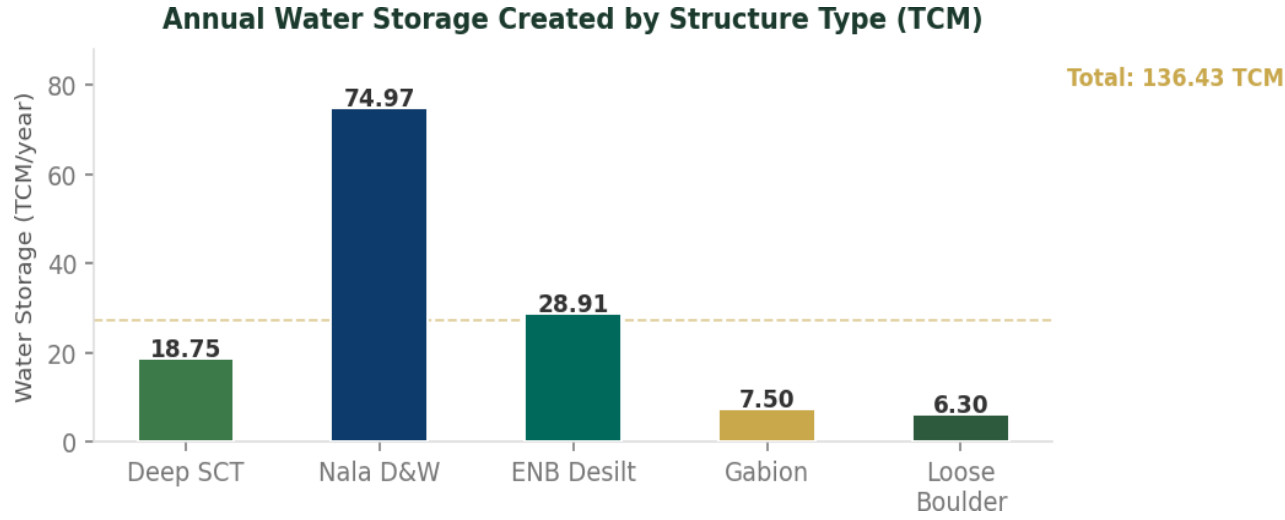

OUTCOMES & MEASURABLE IMPACT

GROUNDWATER RECHARGE	**2.5 – 3.2 METRE** AVERAGE POST-MONSOON RISE OBSERVED ACROSS **21 MONITORING WELLS** IN GHATDARE. PEAK RECHARGE RECORDED JULY–OCTOBER 2025. HIGHEST RECHARGE ZONES ADJACENT TO NALA DEEPENING AND ENB DESILTING SITES.
WATER STORAGE CREATED	TOTAL ADDITIONAL ANNUAL WATER STORAGE OF **136.43 TCM** CREATED — PROVIDING GROUNDWATER RECHARGE AND RELIABLE IRRIGATION BUFFER ACROSS THE ENTIRE 647 HA WATERSHED AREA.
IRRIGATION POTENTIAL	SIGNIFICANT IMPROVEMENT IN IRRIGATION POTENTIAL WITH **100 HA** DIRECTLY UNDER ASSURED IRRIGATION; PROGRESSIVE EXPANSION TOWARD THE 647 HA LONG-TERM TARGET AS TREATMENT ZONES MATURE.
SOIL EROSION CONTROL	EROSION STABILISED ACROSS TREATED RIDGE-TO-VALLEY ZONES. GULLY PLUGGING EFFECTIVE — **5 GABION** AND **30 LOOSE BOULDER** STRUCTURES SUCCESSFULLY INSTALLED AND FUNCTIONAL.
WATER PURIFICATION UNIT	UNIT PLANNED AND **PROCUREMENT INITIATED**. ONCE COMMISSIONED, WILL PROVIDE TREATED SAFE DRINKING WATER TO ALL 225 HOUSEHOLDS IN GHATDARE VILLAGE.
COMMUNITY GOVERNANCE	**MAJORITY GRAM SABHA APPROVAL** SECURED. ALL 225 HOUSEHOLDS ENGAGED VIA COMMUNITY SESSIONS AND LOCAL COMMITTEES FORMED FOR LONG-TERM MAINTENANCE OF WATERSHED STRUCTURES.

GROUNDWATER MONITORING — JUNE 2025 TO APRIL 2026

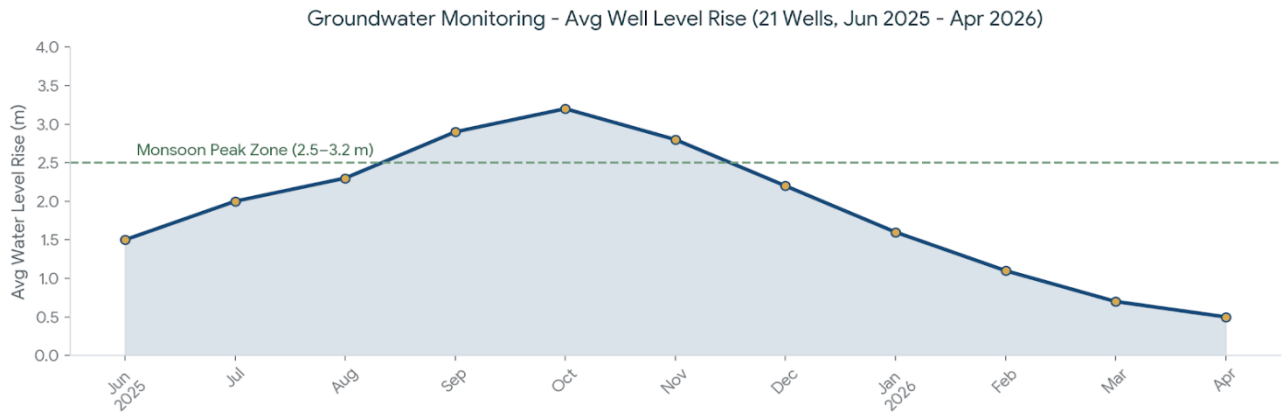

Parameter	Detail
Monitoring Points	21 observation wells across Ghatdare village
Average Well Depth	8 – 9 metres
Post-monsoon Rise	Average 2.5 – 3.2 m (July–October 2025)
Seasonal Low	February–March 2026 (dry season)
GPS Coverage	Lat 18.0157–18.0186 | Long 74.0693–74.0712
Highest Recharge Zones	Adjacent to Nala Deepening & ENB desilting sites

FIELD DOCUMENTATION – NALA DEEPENING & EARTHWORK

Field photographs of Nala deepening and widening operations at Ghatdare using Tata Hitachi excavators — core earthwork activity achieving 24,990 m³ against the 25,000 m³ target.



Tata Hitachi Excavator — Active Nala Deepening (24,990 m³)


Completed Nala Section — Soil Excavation Site


Nala Widening — Field View


DesiltingTreatment


Gabion Measurement

FIELD DOCUMENTATION —
AERIAL VIEW



Aerial View — Completed Nala Deepening with Water Ponds, Ghatdare (Drone Photo)





FIELD DOCUMENTATION —
AERIAL VIEW







FIELD DOCUMENTATION - LAUNCH & COMMUNITY



TE Connectivity × SJSM Project Launch — Ghatdare Site


Gram Sabha — Farmer Community Meeting


Field Visits

WATER PURIFICATION UNIT - SAFE DRINKING WATER

THE WATER PURIFICATION UNIT — A KEY DELIVERABLE OF THE TE IWMP — WAS PROCURED AND INSTALLED TO PROVIDE SAFE, TREATED DRINKING WATER TO ALL 225 HOUSEHOLDS OF GHATDARE VILLAGE. THE UNIT WAS INAUGURATED AND RECEIVED ENTHUSIASTICALLY BY THE COMMUNITY, PARTICULARLY WOMEN AND SHG MEMBERS WHO LED THE COMMISSIONING PROCESS.



Water Purification Plant — Inauguration by Community



Inauguration and Handover session

WATER PURIFICATION UNIT — KEY FACTS

CAPACITY: COMMUNITY-SCALE R.O PURIFICATION

SYSTEM BENEFICIARIES: ALL 225 HOUSEHOLDS, GHATDARE VILLAGE

TECHNOLOGY: REVERSE OSMOSIS WITH MULTI-STAGE FILTRATION

STATUS: **INSTALLED AND COMMISSIONED** — COMMUNITY OPERATIONS UNDERWAY.

IMPACT: PROVIDES CLEAN, SAFE DRINKING WATER, REDUCING WATERBORNE DISEASE RISK

MEDIA COVERAGE NEWSPAPER REPORTS

The TE Integrated Watershed Management Project attracted significant regional media attention and coverage in 5 major Marathi newspapers — *Pudhari* (district-wide circulation), Tarun Bharat, Sahas Varta, *Dainik Muktagiri, Navrastra*— reaching thousands of readers across Satara and Khandala Taluka, building public awareness of watershed conservation and CSR impact.

दैनिक साहस वार्ता

संपादक : श्री. श्रीकांत शिवलाय मुळे



पाणलोट विकास प्रकल्पातून साकारणार शेतीसिंचनाचा मार्ग

घाटदरे येथे जलसंधारण कामे, सामाजिक संस्थांची बांधिलकी

साहस वार्ता

खंडाळा : खंडाळा तालुक्याच्या दक्षिणेकडील घाटदरे गाव हे नेहमीच पाण्यासाठी दुर्भिक्ष असलेले गाव. गावात पाणीसाठवण क्षमता वाढविल्याशिवाय जमिनीची पाणीपातळी वाढणार नाही. यासाठी टीई कनेक्टिव्हीटी आणि श्रमजीवी सामाजिक संस्था यांच्या माध्यमातून पाणलोट विकास प्रकल्प राबवून पाणी अडविण्यात येणार आहे. या प्रकल्पामुळे लाखो लीटर पाणी साठवण होणार असून गावच्या माथी असणारा दुष्काळी कलंक पुसून गाव जलस्वयंपूर्ण बनेल. त्यामुळे परिसरातील शेकडो हेक्टर शेती सिंचनाखाली येणार आहे.

घाटदरे - भोसलेवाडीत दरवर्षीच पाण्याची टंचाई भासते. शेतीसिंचनाबरोबर पिण्याच्या पाण्याचीही मोठी समस्या भेडसावते. त्यासाठी गावच्या परिसरात पाणीसाठवण बंधारे बांधणे गरजेचे आहे हे जाणून घेऊन ग्रामस्थांनी टीई कनेक्टीव्हीटी व श्रमजीवी संस्थेशी संपर्क साधला.

संस्थेच्या माध्यमातून गावच्या परिसरातील ओढा खोलीकरण, तलावातील गाळ काढणे, लूज बोल्डर, सीसीटी बंधारे, डोंगर ओघळीमध्ये दगडी बांध, समतल चर अशा प्रकारची कामे हाती घेण्यात आली

गावात जलसंधारण कामासाठी संस्थेच्या मदतीने काम करण्याचे ठरविले आहे. त्यांना गावासाठी पाण्याची गरज पटवून दिली. त्यांनी सामाजिक बांधिलकी लक्षात घेऊन उपक्रम हाती घेतला आहे. यासाठी गावकऱ्यांचे सर्वोतोपरी सहकार्य राहील. सामाजिक भावनेने सुरू केलेल्या कामाचा आम्हाला निश्चित आनंद आहे.

- शिवाजी सोळसकर, घाटदरे

आहेत. या प्रकल्पाद्वारे लाख लिटर पाणी साठवण होवून सुमारे ६४७ हेक्टर शेती सिंचनाखाली येणार आहे. गावच्या परिसरात पाणी साठवण अधिक प्रमाणात होणार असल्यामुळे पिण्याच्या पाण्यासाठी व शेतीच्या पाण्यासाठी याचा मोठा फायदा होणार आहे. जलसंधारणाच्या या कामाचा प्रारंभ टीईचे संचालक अनिल राय, जुही जयनंदन, कनिष्ठा शर्मा, प्रज्ञा शिवेकर, विदया सिदमल, कल्पना ढोरे, संजय होन, अजय सिंग, शिवाजी कुपते तसेच श्रीमजीवी संस्थेचे कार्याध्यक्ष राम कोळेकर, मोहन खराडे, सुरेश कदम, नौशाद मुलाणी, इंद्रजित माने, सरपंच रेखा इंदलकर, उपसरपंच धनंजय सोळसकर, शिवाजी सोळसकर यांच्या हस्ते झाला. यावेळी ग्रामस्थ मोठया संख्येने उपस्थित होते.

दैनिक मुक्तागिरी

पाणलोट विकास प्रकल्पातून साकारणार शेतीसिंचनाचा मार्ग

घाटदरे येथे जलसंधारण कामे; सामाजिक संस्थांची बांधिलकी



मुक्तागिरी वृत्तसेवा

खंडाळा, दि. ५ : खंडाळा तालुक्याच्या दक्षिणेकडील घाटदरे गाव हे नेहमीच पाण्याचे दुर्भिक्ष असलेले गाव. गावात पाणी साठवण क्षमता वाढविल्याशिवाय जमिनीची पाणीपातळी वाढणार नाही;यासाठी टीई कनेक्टिव्हीटी आणि श्रमजीवी सामाजिक संस्था यांच्या माध्यमातून पाणलोट विकास प्रकल्प राबवून पाणी अडविण्यात येणार आहे. या प्रकल्पामुळे लाखो लीटर पाणी साठवण होणार असून गावच्या माथी असणारा दुष्काळी कलंक पुसून गाव जलस्वयंपूर्ण बनेल. त्यामुळे परिसरातील शेकडो हेक्टर शेती सिंचनाखाली येणार आहे.

घाटदरे - भोसलेवाडीत दरवर्षीच पाण्याची टंचाई भासते. शेतीसिंचनाबरोबर पिण्याच्या पाण्याचीही मोठी समस्या भेडसावते. त्यासाठी गावच्या परिसरात पाणीसाठवण बंधारे बांधणे गरजेचे आहे.

जाणून घेऊन ग्रामस्थांनी टीई कनेक्टीव्हीटी व श्रमजीवी संस्थेशी संपर्क साधला.

संस्थेच्या माध्यमातून गावच्या परिसरातील ओढा खोलीकरण, तलावातील गाळ काढणे, लूज बोल्डर , सीसीटी बंधारे, डोंगर ओघळीमध्ये दगडी बांध, समतल चर अशा प्रकारची कामे हाती घेण्यात आली आहेत. या प्रकल्पाद्वारे लाख लिटर पाणी साठवण होवून सुमारे ६४७ हेक्टर शेती सिंचनाखाली येणार आहे. गावच्या परिसरात पाणी साठवण अधिक प्रमाणात होणार असल्यामुळे पिण्याच्या पाण्यासाठी व शेतीच्या पाण्यासाठी याचा मोठा फायदा होणार आहे.

जलसंधारणाच्या या कामाचा प्रारंभ टीईचे संचालक अनिल राय, जुही जयनंदन, कनिष्ठा शर्मा, प्रज्ञा शिवेकर, विदया सिदमल, कल्पना ढोरे, संजय होन, अजय सिंग, शिवाजी कुपते तसेच श्रीमजीवी संस्थेचे कार्याध्यक्ष राम कोळेकर, मोहन खराडे, सुरेश कदम, नौशाद मुलाणी, इंद्रजित माने, सरपंच रेखा इंदलकर, उपसरपंच धनंजय सोळसकर, शिवाजी सोळसकर यांच्या हस्ते झाला. यावेळी ग्रामस्थ मोठया

नवराष्ट्र

www.navarashtra.com

श्रमजीवी संस्थेच्या पुढाकारातून जलसंधारणेची कामे हाती ; ग्रामपंचायतीच्या सहकार्यातून राबविला प्रकल्प

घाटदरे पाणलोट विकास प्रकल्पाचा प्रारंभ



खंडाळा, (वा.) गावाच्या शेती पाण्याची समस्या सोडविण्यासाठी तालुक्यातील घाटदरे येथे पाणलोट विकास प्रकल्पाचा प्रारंभ करण्यात आला. टी. ई. कनेक्टीव्हीटी कंपनी व साताऱ्यातील श्रमजीवी संस्था यांच्या संयुक्त विद्यमाने ग्रामपंचायत घाटदरे - भोसलेवाडी ग्रामपंचायतीच्या सहकार्याने एकात्मिक पाणलोट विकास प्रकल्प राबविण्यात येत आहे. गावात २२५ कुटूंब असून ६४७ हेक्टर जमिनीचे क्षेत्र आहे. या गावात कंपनी व श्रमजीवी संस्थेच्या पुढाकाराने जलसंधारणाची कामे हाती घेण्यात आली आहेत.

या प्रकल्पाचे उद्घाटन टी. ई. कनेक्टीव्हीटी कंपनीचे डायरेक्टर अनिल राय यांच्यासह मान्यवरांच्या हस्ते करण्यात आले. दरम्यान, सामाजिक दायित्वाची भूमिक घेत गावामध्ये जलसंधारणाची कामे घेतली आहेत. त्याचा गावाला नक्कीच फायदा होईल,असा विश्वास कंपनीचे शिवाजी कुपते यांनी व्यक्त केला.

यावेळी जुही जयनंदन,अजय सिंग, कनिष्ठा शर्मा, संजय होन, शिवाजी कुपते, प्रज्ञा शिवेकर, विद्या सिदमल, कल्पना ढोरे श्रमजीवी संस्थेचे कार्याध्यक्ष श्रीराम कोळेकर, मोहन खराडे, सुरेश कदम, नौशार मुलाणी, इंद्रजित माने यांच्यासह ग्रामस्थ उपस्थित होते. प्रास्ताविक सुरेश कदम यांनी केले. शिवाजी सोळसकर यांनी आभार मानले.

'जलसंधारण'मुळे शिवारात ३१५.२४ टी.सी.एम. पाणीसाठा वाढेल

जलसंधारणाच्या कामांमुळे भूगर्भातील पाणी पातळी वाढविणे, जमिनीची होणारी धूप थांबविणे, शेती पिकांचे उत्पन्न वाढवणे, गावाला शुद्ध पिण्याचे पाणी उपलब्ध करून देणे या बरोबरच शिवारात जलसंधारणाच्या कामातून सुमारे ३१५.२४ टी.सी.एम.एवढा पाणीसाठा वाढेल असा विश्वास व्यक्त करण्यात येत आहे. यामध्ये नालाखोलीकरण, तळ्यातील गाळ काढणे, लूज बोल्डर, जाळी बंधारे, सलग समतल चर आदी कामांबरोबर गावाला जलशुन्दरीकरण केंद्राचा समावेश आहे.

तरुण भारत संवाद



घाटदरे : पाणलोट विकास कामांचा शुभारंभ करताना मान्यवर (छाया : निलेश गायकवाड)

घाटदरे येथे पाणलोट विकास प्रकल्पाचा शुभारंभ

प्रतिनिधी

खंडाळा

गावाच्या शेती पाण्याची समस्या सोडविण्यासाठी तालुक्यातील घाटदरे येथे पाणलोट विकास प्रकल्पाचा शुभारंभ करण्यात आला. टी. ई. कनेक्टीव्हीटी कंपनी व साताऱ्यातील श्रमजीवी संस्था यांच्या संयुक्त विद्यमाने ग्रामपंचायत घाटदरे--भोसलेवाडी ग्रामपंचायतीच्या सहकार्याने एकात्मिक पाणलोट विकास प्रकल्प राबविण्यात येत आहे. गावात २२५ कुटूंब असून ६४७ हेक्टर जमिनीचे क्षेत्र आहे. या गावात कंपनी व श्रमजीवी संस्थेच्या पुढाकाराने जलसंधारणाची कामे हाती घेण्यात आली आहेत. त्यामध्ये भूगर्भातील पाणी पातळी वाढविणे, जमिनीची, होणारी धूप थांबविणे, शेती पिकांचे उत्पन्न वाढवणे, गावाला शुद्ध पिण्याचे पाणी उपलब्ध करून देणे या बरोबर शिवारात जलसंधारणाच्या कामातून सुमारे ३१५.२४ टी.एम.सी. एवढा पाणी साठा वाढेल असा विश्वास व्यक्त करण्यात येत आहे. यामध्ये नालाखोलीकरण, तळ्यातील गाळ काढणे, लूज बोल्डर, जाळी बंधारे, सलग समतल चर आदी कामांबरोबर गावाला जलशुद्धीकरण केंद्राचा समावेश आहे.

या प्रकल्पाचे उद्घाटन टी. ई. कनेक्टीव्हीटी कंपनीचे डायरेक्टर अनिल राय यांच्यासह मान्यवरांच्या हस्ते करण्यात आले. दरम्यान, सामाजिक दायित्वाची भूमिका घेत गावामध्ये जलसंधारणाची कामे घेतली आहेत. त्याचा गावाला नक्कीच फायदा होईल, असा विश्वास कंपनीचे शिवाजी कुपते यांनी व्यक्त केला.

यावेळी जुही जयनंदन, अजय सिंग, कनिष्ठा शर्मा, संजय होन, शिवाजी कुपते, प्रज्ञा शिवेकर, विद्या सिदमल, कल्पना ढोरे श्रमजीवी संस्थेचे कार्याध्यक्ष श्रीराम कोळेकर, मोहन खराडे, सुरेश कदम, नौशार मुलाणी, इंद्रजित माने यांच्यासह ग्रामस्थ उपस्थित होते.

याप्रसंगी कार्यक्रमाचे प्रास्ताविक सुरेश कदम यांनी केले. शेवटी सर्व उपस्थितांचे शिवाजी सोळसकर यांनी आभार मानले.

पुढारी

घाटदरेत पाणलोट विकास प्रकल्पाचा शुभारंभ



पाणलोट विकास प्रकल्पाच्या शुभारंभप्रसंगी ग्रामस्थांना मार्गदर्शन करताना संस्थेचे पदाधिकारी.

खंडाळा : पुढारी वृत्तसेवा

गावाच्या शेती पाण्याची समस्या सोडवण्यासाठी खंडाळा तालुक्यातील घाटदरे येथे पाणलोट विकास प्रकल्पाचा शुभारंभ करण्यात आला. टी. ई. कनेक्टीव्हीटी कंपनी व साताऱ्यातील श्रमजीवी संस्था यांच्या संयुक्त विद्यमाने ग्रामपंचायत घाटदरे - भोसलेवाडी ग्रामपंचायतीच्या सहकायने एकात्मिक पाणलोट विकास प्रकल्प राबवण्यात येत आहे.

गावात २२५ कुटूंब असून ६४७ हेक्टर जमिनीचे क्षेत्र आहे. या गावात कंपनी व श्रमजीवी संस्थेच्या पुढाकाराने जलसंधारणाची कामे हाती घेण्यात आली आहेत. त्यामध्ये भूगर्भातील पाणी पातळी वाढवणे, जमिनीची होणारी धूप थांबवणे, शेती पिकांचे उत्पन्न वाढवणे,गावाला शुद्ध पिण्याचे पाणी उपलब्ध करून देणे या बरोबर शिवारात जलसंधारणाच्या कामातून पाणीसाठा वाढवण्याचे उद्दिष्ट आहे.

या प्रकल्पाचे उद्घाटन कंपनीचे डायरेक्टर अनिल राय यांच्यासह मान्यवरांच्या हस्ते करण्यात आले. यावेळी जुही जयनंदन,अजय सिंग, कनिष्ठा शर्मा, संजय होन, शिवाजी कुपते, प्रज्ञा शिवेकर , विद्या सिदमल , कल्पना ढोरे श्रमजीवी संस्थेचे कार्याध्यक्ष श्रीराम कोळेकर,मोहन खराडे,सुरेश कदम,नौशार मुलाणी, इंद्रजित माने यांच्यासह ग्रामस्थ उपस्थित होते.

ALIGNMENT WITH UN SUSTAINABLE DEVELOPMENT GOALS

The TE IWMP directly contributes to **six UN Sustainable Development Goals**, demonstrating how integrated watershed management creates multi-dimensional social, environmental, and governance impact.



Improves groundwater recharge and purification to ensure safe drinking water for 225 households.



Expands assured irrigation across 647 Ha to boost agricultural productivity and food security for farm families.



Builds resilience through soil water conservation, water harvesting, and sustainable land management practices.



Controls soil erosion, restores degraded land, and promotes sustainable ecosystem use across the watershed.



Multi-stakeholder collaboration: TE Connectivity (CSR), SJSM (NGO) Gram Panchayat (governance). ,

CONCLUSION & WAY FORWARD

The TE Integrated Watershed Development Project – Ghatdare delivered **measurable outputs** (structures, desilting, monitoring, community mobilisation) and achieved **early outcomes** (substantial groundwater recharge of 2.5–3.2 m, 136.43 TCM additional water storage, improved irrigation potential, and strengthened community governance) in FY 2025-26.

Next Steps: Completing community-led maintenance systems, scaling irrigation interventions to reach the full 647 Ha target, measuring crop yield changes, and commissioning the Water Purification Unit will consolidate these gains and demonstrate long-term impact aligned with SDGs 2, 6, 13, 15, and 17.

TE Integrated Watershed Management Project (IWMP) — Ghatdare CSR

Partner: TE Connectivity | Implementing Partner: SJSM, Satara

Head Operations : Mr. Ram Kolekar | Location: Ghatdare, Khandala, Satara

Annual Report FY 2025-26 | Report prepared: April 202

6
